

Force Main

Bid Package 13 – This contract has been completed

*Master Pump Station*

Bid Package 14 (Widell, Inc.) – Widell Inc. has completed the construction. They are working on completion of the Substantial Completion punch list. A 21 day time extension has been requested.

*W-15 Force Main*

Bid Package 15 – The design for this project is complete and the bid package was delivered to the City of Hollywood. The City has placed this project on hold.

*Snake Warrior's Island Plantings & Mitigation*

Bid Package 16 (Native Technologies, Inc.) – has completed the construction portion of this project and final payment has been made. Monitoring reports will be prepared for the next four years.


*Pembroke Road*

This contract has been completed

# NORTH ANDREWS GARDENS NIP

The North Andrews Gardens Neighborhood Improvement Project (NAGNIP) includes 712 acres, 9,000 residents, 2,600 septic tanks, and 3,600 homes. The planned improvements include 29 miles of roadways, 83 miles of pipe, and 53 miles of sidewalk. The area is bounded by Cypress Creek Road (NE 62<sup>nd</sup> Street), Interstate 95 (I-95), Prospect Road, and NE 6<sup>th</sup> Avenue / NE 9<sup>th</sup> Avenue and is divided into 8 construction bid packages.

## Project Location Map

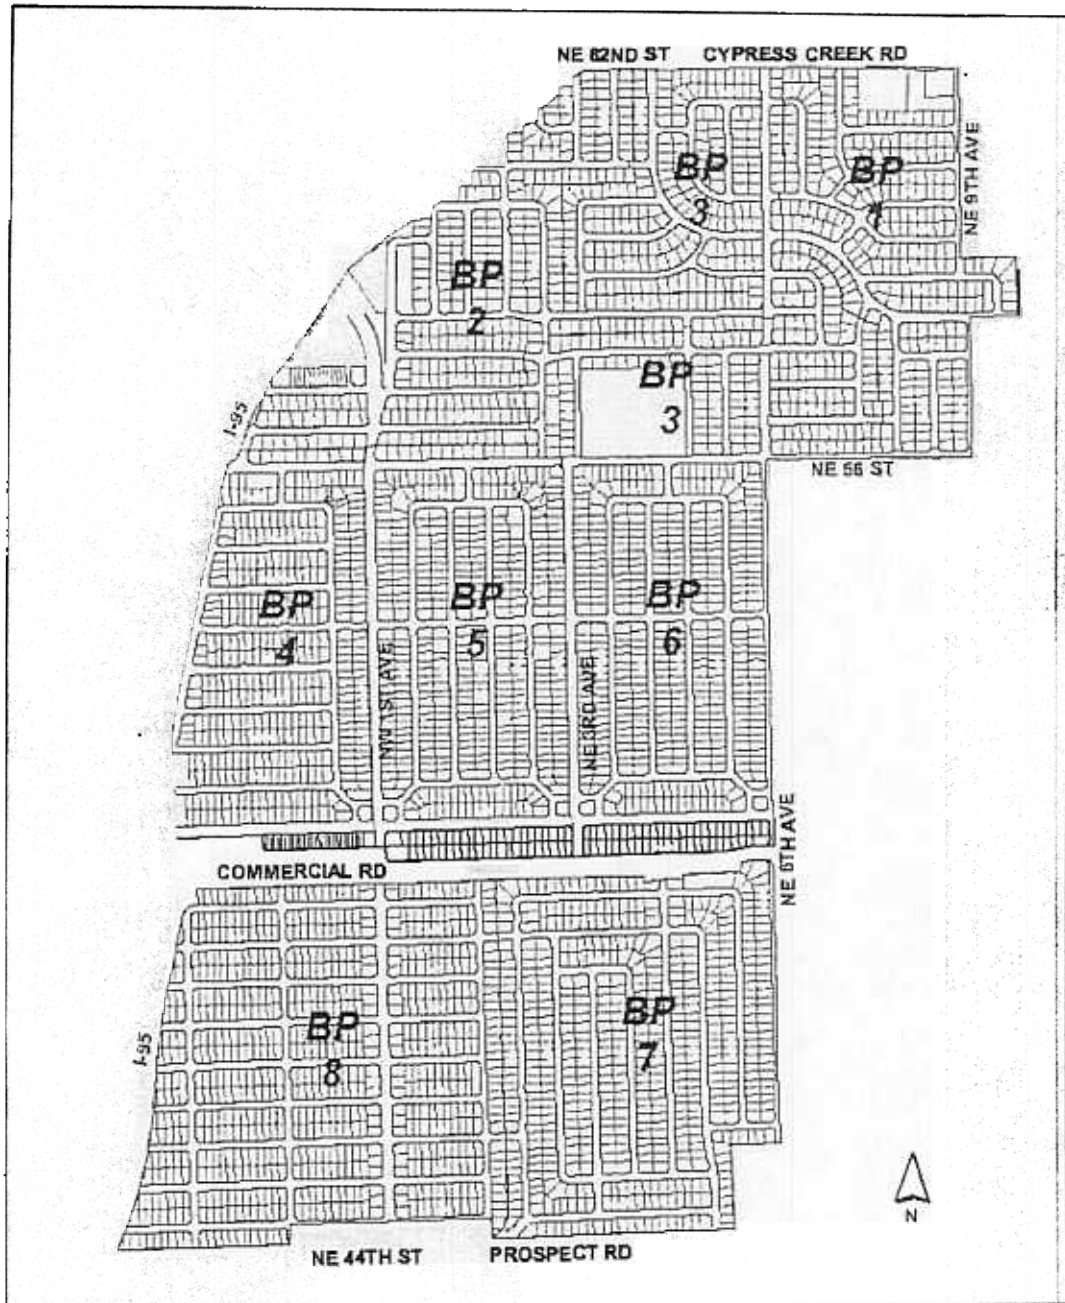

## *North Area*

Bid Package 1 (Russell Engineering, Inc.) – This project started on June 14, 1999, and was substantially completed on May 21, 2001; however, the contractor is subject to liquidated damages until defective and uncompleted work has been finalized. The current contract price is \$4,549,831.

Bid Package 2 (Ric Man International, Inc.) – This project started on June 26, 2000, and was substantially completed on May 1, 2002; however, the contractor is subject to liquidated damages until final completion. The micro-tunneling work under I-95 encountered problems and will be deleted from this contract. The current contract price is \$6,044,553.

Bid Package 3 (Man Con, Inc.) – This project started on August 1, 2001, and is ahead of schedule. The current contract price is \$8,511,371. The contractor has used 37% of the contract time and has earned 84% of the total contract price. The project is scheduled to be completed in the 4<sup>th</sup> quarter of 2003.

## *Central Area*

Bid Package 4 – This project is scheduled to start construction in the 2<sup>nd</sup> quarter of 2003, and be completed in the 4<sup>th</sup> quarter of 2004.

Bid Package 5 (Douglas N. Higgins, Inc.) – This project started on September 10, 2001, and is currently behind schedule. The current contract price is \$9,371,019. The contractor has used 56% of the contract time and has earned 37% of the total contract price. The project is scheduled to be completed on September 22, 2003.

Bid Package 6 – This project is scheduled to start construction on June 23, 2003, and be completed on December 13, 2004.

## *South Area*

Bid Package 7 – This project is scheduled to start construction in the 4<sup>th</sup> quarter of 2003, and be completed in 2<sup>nd</sup> quarter of 2005. The City of Oakland Park indicated they will retain ownership of their water distribution system; consequently, the City will be required to improve their water system in the right-of-way prior to the NIP construction.

Bid Package 8 – This project is scheduled to start construction in the 2<sup>nd</sup> quarter of 2003, and be completed in the 4<sup>th</sup> quarter of 2005. The City of Oakland Park indicated they will retain ownership of their water distribution system; consequently, the City will be required to improve their water system in the right-of-way prior to the NIP construction.
